



Date June 03, 2024

ACCEPTING COMPLETED CONSTRUCTION AND APPROVING FINAL PAYMENT FOR ANIMAL CONTROL FACILITY BID PACKAGE NO. 17 - LANDSCAPING, ALPHA LANDSCAPES LLC

BE IT RESOLVED BY THE CITY COUNCIL OF THE CITY OF DES MOINES, IOWA: That the attached report of the Des Moines City Engineer, showing the cost of the construction of the Animal Control Facility Bid Package No. 17 - Landscaping, Activity ID 102022018, in accordance with the contract approved between Alpha Landscapes LLC, Riley Marvin, Owner, 5145 NW Beaver Drive, Johnston, IA, 50131, under Roll Call No. 22-0488, of March 21, 2022, and the City of Des Moines, and recommending the acceptance thereof, be and the same is hereby approved, and accepted.

BE IT FURTHER RESOLVED: That \$150,486.90 is the total cost, of which \$145,972.29 has been paid the Contractor, and \$0.00 is now due and is hereby approved as final partial payment for the above project, the remaining balance of \$4,514.61 is to be paid at the end of thirty days, with funds retained for unresolved claims on file in accordance with Iowa Code Chapter 573.

BE IT FURTHER RESOLVED: That the Director of Finance be and is hereby authorized to release said retainage if suit is not filed as above provided.

Moved by _____ to adopt. Second by _____

FORM APPROVED:

FUNDS AVAILABLE:

s/Kathleen Vanderpool

Nickolas J. Schaul

Kathleen Vanderpool
Deputy City Attorney

Nickolas J. Schaul
Director of Finance

SLN pw

Funding Source: 2024-25 CIP, Page 30, Animal Control Facility, BL130

Table with 5 columns: COUNCIL ACTION, YEAS, NAYS, PASS, ABSENT. Rows include BOESEN, COLEMAN, GATTO, MANDELBAUM, SIMONSON, VOSS, WESTERGAARD, and TOTAL.

MOTION CARRIED APPROVED

Mayor


CERTIFICATE

I, Laura Baumgartner, City Clerk of said City hereby certify that at a meeting of the City Council of said City of Des Moines, held on the above date, among other proceedings the above was adopted.

IN WITNESS WHEREOF, I have hereunto set my hand and affixed my seal the day and year first above written.

City Clerk

10A

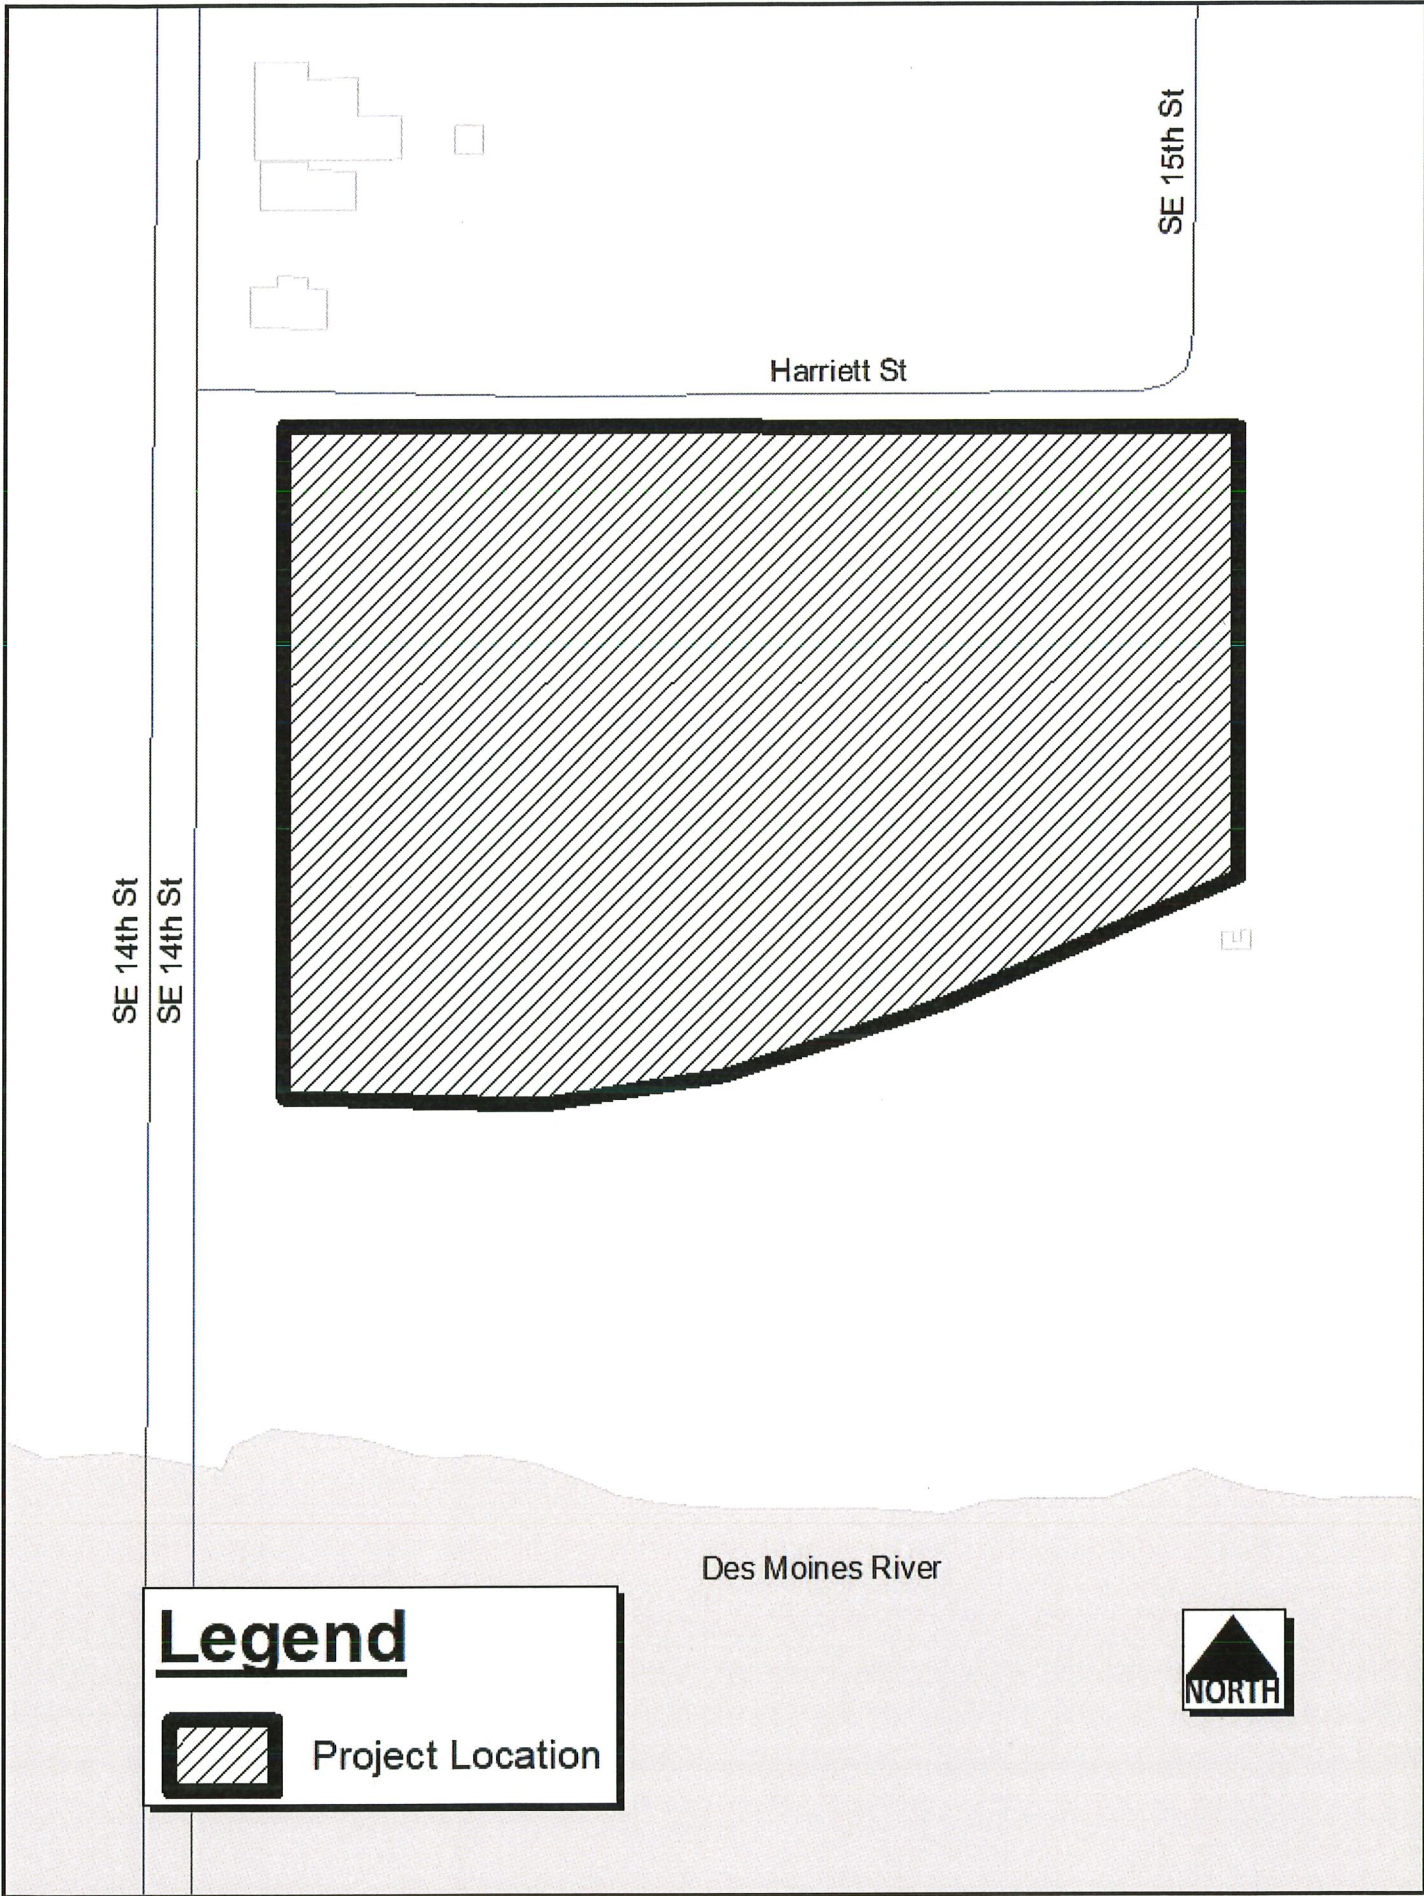


SE 14th St
SE 14th St


Harriett St

SE 15th St

Des Moines River

Legend

 Project Location





PROJECT SUMMARY

Animal Control Facility Bid Package No. 17 - Landscaping

Activity ID 102022018

On March 21, 2022, under Roll Call No. 22-0488, the Council awarded the contract for the above improvements to Alpha Landscapes LLC, in the amount of \$145,950.00. Tabulated below is a history of project change orders.

Change Order No.	Initiated By	Description	Amount
1	City	11/28/2023 Add project changes found as per PCO-056.	\$3,936.90
2	City	2/5/2024 Add project changes found as per PCO-077.	\$600.00
Original Contract Amount			\$145,950.00
Total Change Orders			\$4,536.90
Percent of Change Orders to Original Contract			3.11%
Total Contract Amount			\$150,486.90

10A

Department of Engineering
City of Des Moines, Iowa



June 3, 2024

CERTIFICATION OF COMPLETION

AGENDA HEADING:

Accepting completed construction and approving final payment for the Animal Control Facility Bid Package No. 17 - Landscaping, Alpha Landscapes LLC.

SYNOPSIS:

Approve the Engineer's Certification of Completion, accept construction of said improvement, and authorize final payment to the contractor.

FISCAL IMPACT:

Amount: \$150,486.90 As-Built Contract Cost
Funding Source: 2024-25 CIP, Page 30, Animal Control Facility, BL130

CERTIFICATION OF COMPLETION:


On March 21, 2022, under Roll Call No. 22-0488, the City Council awarded a contract to Alpha Landscapes LLC, Riley Marvin, Owner, 5145 NW Beaver Drive, Johnston, IA 50131 for the construction of the following improvement:

Animal Control Facility Bid Package No. 17 - Landscaping, 102022018

The improvement includes new construction of an approximately 21,900 square feet animal care and control facility which includes animal intake and service areas, adoption service areas, animal housing, veterinary clinic with surgery, and drive-thru sally port; design consists of brick masonry base, metal panel and cedar siding, glazed aluminum storefront and windows; wall structure consists of perimeter bearing stud walls and internal steel columns and bearing concrete masonry walls; floor structure is concrete slab-on-grade; roof structure is metal roof joists and decking; roofing system is a single-ply fully adhered membrane on low slope roof areas; Portland Cement Concrete (PCC) parking lots, PCC sidewalks, sanitary sewer, sanitary sewer manholes, water main, fiber and conduit, chain link fenced outdoor dog runs, surface restoration, and other incidental items; all in accordance with the contract documents associated with Bid Package No. 17 – Landscaping, including Plan File No. 633-001/218, located at 1441 Harriet Street, Des Moines, Iowa.

I hereby certify that the construction of said Animal Control Facility Bid Package No. 17 - Landscaping, Activity ID 102022018, has been completed in substantial compliance with the terms of said contract, and I hereby recommend that the work be accepted. The work commenced on July 11, 2022, and was completed on May 10, 2024.

I further certify that \$150,486.90 is the total cost of said improvement, of which \$145,972.29 has been paid the Contractor and \$0.00 is now due and is hereby approved as final partial payment for the above project, the remaining balance of \$4,514.61 is to be paid at the end of thirty days, with funds retained for unresolved claims on file in accordance with Iowa Code Chapter 573. The amount of completed work is shown on the attached Estimate of Construction Completed.


Steven L. Naber, P.E.
Des Moines City Engineer

10A

ENGINEERING DEPARTMENT
CITY OF DES MOINES, IOWA



ESTIMATE OF CONSTRUCTION COMPLETED

PARTIAL PAYMENT NO. 6 - FINAL

PROJECT: ANIMAL CONTROL FACILITY BID PACKAGE #17-Landscaping
CONTRACTOR: ALPHA LANDSCAPES LLC

Proj No: N/A
Activity ID: 10-2022-018
Date: 05/10/2024

LINE NO.	DESCRIPTION	UNIT	UNITS			UNIT PRICE	TOTAL AMOUNT
			ESTIMATED	AUTHORIZED	CONSTRUCTED TO DATE		
1	MOBILIZATION	LS	1.000	1.000	1.000	24,000.00	\$24,000.00
2	CONSTRUCTION	LS	1.000	1.000	1.000	121,950.00	\$121,950.00
1001	PCO-056 - Replace Lawn with Trap Rock at Secure Parking	LS	0.000	1.000	1.000	3,936.90	\$3,936.90
2001	PCO-077 - Modify Edging at Added Handhole per ASI-3R	LS	0.000	1.000	1.000	600.00	\$600.00
TOTAL CONTRACT AMOUNT PLUS CHANGE ORDERS			\$150,486.90				
PARTIAL PAYMENT NO. 1			\$115,119.60				
PARTIAL PAYMENT NO. 2			\$18,543.39				
PARTIAL PAYMENT NO. 3			\$9,302.30				
PARTIAL PAYMENT NO. 4			\$582.00				
PARTIAL PAYMENT NO. 5			\$2,425.00				
THIS PARTIAL PAYMENT			\$0.00				
TOTAL PARTIAL PAYMENTS			\$145,972.29				
BALANCE			\$4,514.61				
			100%				

PREPARED BY: John Keenan

CHECKED BY: _____

TOTAL	\$150,486.90
RETAINAGE	\$4,514.61
TOTAL LESS RETAINAGE	\$145,972.29
LESS PREVIOUS PAYMENT	\$145,972.29
AMOUNT DUE	\$0.00

PARTIAL PAYMENT NO. 6 - FINAL
